Project :- New Mixing Plant

ID	Task Name	Duration	Start	Finish
1	**Project Ref:- PXXXX rev 0**	113 days	Mon 07/02/11	Mon 25/07/11
2				
3	Contractual & Commercial	**5 days**	**Mon 07/02/11**	**Fri 11/02/11**
4	Order Placement	1 day	Mon 07/02/11	Mon 07/02/11
5	Acknowledge Order	4 days	Tue 08/02/11	Fri 11/02/11
6				
7	Design and Specification	**56 days**	**Mon 14/02/11**	**Wed 11/05/11**
8	Evaluation of Process Data	25 days	Mon 14/02/11	Fri 18/03/11
9	Complete Process Pipework P.& I.D.'s	20 days	Mon 21/02/11	Fri 18/03/11
10	Equipment Specifications	35 days	Mon 14/02/11	Fri 01/04/11
11	General Arrangement Drawing	15 days	Mon 14/03/11	Fri 01/04/11
12	Castor Oil Storage Tank Design and Drawings	5 days	Mon 07/03/11	Fri 11/03/11
13	Manufacturing 2 Pan Disperser Design and Drawings	25 days	Mon 21/02/11	Fri 25/03/11
14	Powder Handling Equipment Design and Drawings	25 days	Mon 21/02/11	Fri 25/03/11
15	Detail Layout Drawings	25 days	Mon 14/03/11	Fri 15/04/11
16	Steelwork / Mezzanine Floor Design and Drawings	10 days	Mon 07/03/11	Fri 18/03/11
17	Pipework Layout Drawing	14 days	Mon 04/04/11	Thu 21/04/11
18	Pipeline Sizing Calculations	4 days	Tue 03/05/11	Fri 06/05/11
19	Pipework Specification	7 days	Tue 03/05/11	Wed 11/05/11
20	Electrical Specification's	7 days	Tue 03/05/11	Wed 11/05/11
21	Control Specification's (F.D.S.)	15 days	Mon 14/03/11	Fri 01/04/11
22				
23	Procurement of Capital Items	**85 days**	**Mon 07/02/11**	**Wed 15/06/11**
24	Steelwork / Mezzanine Floor Fabrication	35 days	Mon 14/03/11	Tue 10/05/11
25	2 Pan Disperser	65 days	Mon 07/02/11	Tue 17/05/11
26	Castor Oil Storage Tank	30 days	Mon 28/03/11	Tue 17/05/11
27	Process Pumps	30 days	Mon 28/03/11	Tue 17/05/11
28	Instrumentation	30 days	Mon 28/03/11	Tue 17/05/11
29	Loadcells	20 days	Mon 11/04/11	Tue 17/05/11
30	Disperser Shaft Wash Vessel	20 days	Mon 11/04/11	Tue 17/05/11
31	Dust Extraction	40 days	Mon 21/03/11	Tue 24/05/11
32	Powder Handling Equipment	70 days	Mon 14/02/11	Wed 01/06/11
33	Process Control - Hardware	40 days	Mon 11/04/11	Wed 15/06/11
34	Process Control - Software	40 days	Mon 11/04/11	Wed 15/06/11
35				
36	Site Work	**48 days**	**Tue 03/05/11**	**Fri 08/07/11**
37	Cast Castor Oil Tank Plinth - Client	5 days	Tue 03/05/11	Mon 09/05/11
38	Cast Weigh Scale Pit - Client	5 days	Tue 03/05/11	Mon 09/05/11
39	Site Establishment and Preliminaries	5 days	Tue 03/05/11	Mon 09/05/11
40	Removal of Existing Castor Oil Tank and Frame	1 day	Tue 10/05/11	Tue 10/05/11
41	Steelwork / Mezzanine Floor Installation	5 days	Tue 10/05/11	Mon 16/05/11
42	Weigh Scale Installation	1 day	Tue 17/05/11	Tue 17/05/11
43	2 Pan Disperser Installation	4 days	Wed 18/05/11	Mon 23/05/11
44	Castor Oil Tank Installation	1 day	Tue 24/05/11	Tue 24/05/11
45	Disperser Shaft Wash Vessel Installation	1 day	Fri 20/05/11	Fri 20/05/11
46	Powder Handling Equipment Installation	10 days	Tue 31/05/11	Mon 13/06/11
47	Install Dust Collection System	5 days	Mon 30/05/11	Mon 06/06/11
48	Process Pumps Installation	1 day	Mon 23/05/11	Mon 23/05/11
49	Construction of Hot Room - Client	5 days	Mon 16/05/11	Fri 20/05/11
50	Relocate Existing Control Panels	5 days	Mon 16/05/11	Fri 20/05/11
51	Electrical Installation	30 days	Mon 23/05/11	Mon 04/07/11
52	Pipework Installation - Process / Services	30 days	Mon 23/05/11	Mon 04/07/11
53	Pipework Lagging, Cladding and Trace Heating	10 days	Mon 27/06/11	Fri 08/07/11
54				
55	Calibration Testing and Commissioning	**8 days**	**Mon 11/07/11**	**Wed 20/07/11**
56	Pipeline Pressure Testing	3 days	Mon 11/07/11	Wed 13/07/11
57	Electrical Testing of Equipment	3 days	Mon 11/07/11	Wed 13/07/11
58	Process Control Commissioning	5 days	Mon 11/07/11	Fri 15/07/11
59	2 Pan Disperser Commisioning	2 days	Mon 18/07/11	Tue 19/07/11
60	Powder Handling Equipment Commisioning	3 days	Mon 18/07/11	Wed 20/07/11
61				
62	Handover	1 day	Mon 25/07/11	Mon 25/07/11

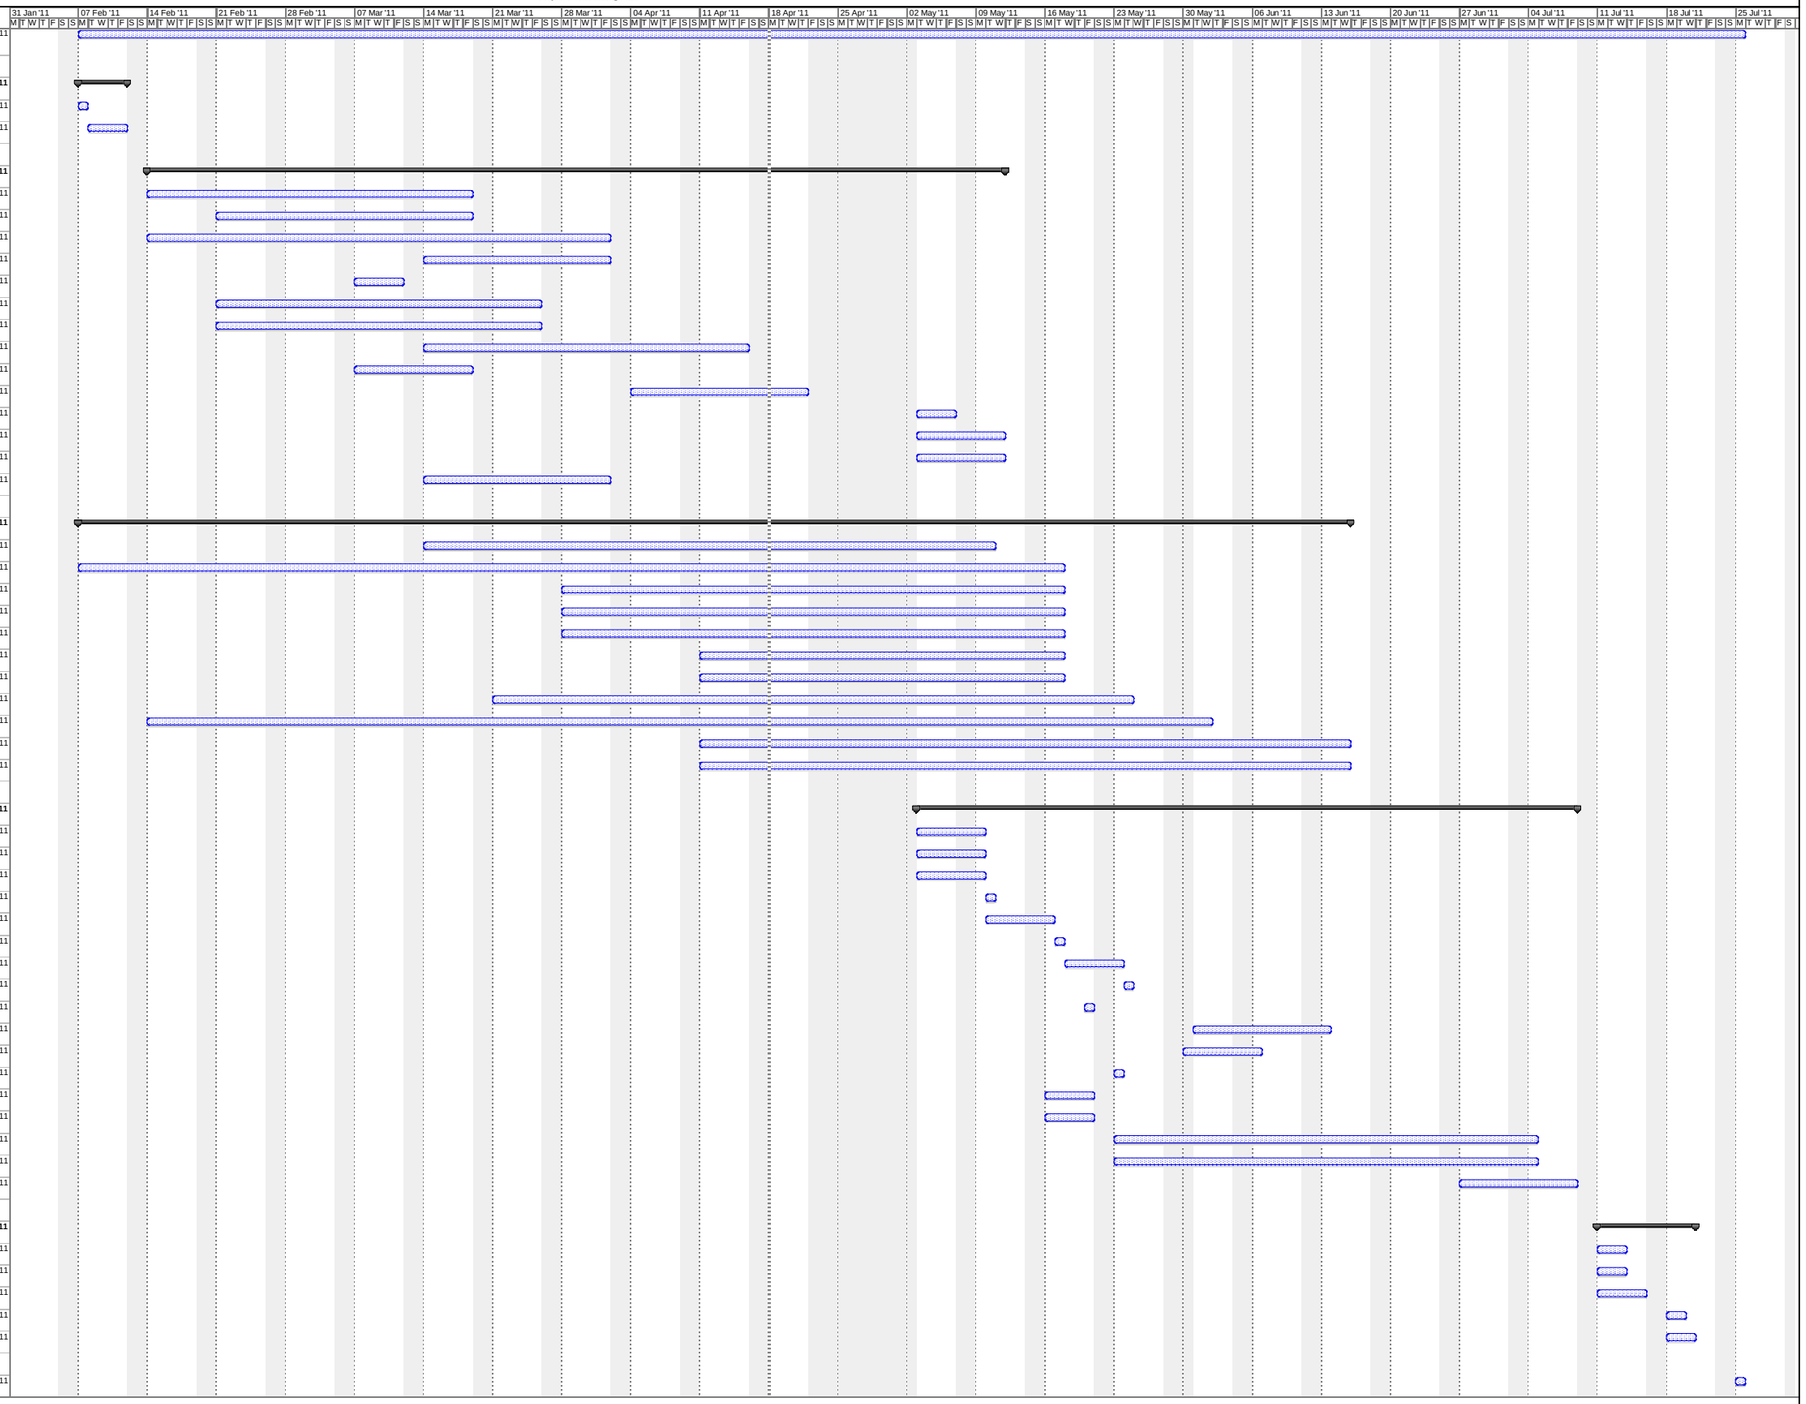

Project :-POW 01 Rev0
Date :-

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline

PDF Created with deskPDF PDF Writer - Trial :: http://www.docudesk.com
